



SMART PROJECTS IN OAKLAND PARK




JUNE 2021



NORTHEAST HIGH SCHOOL

PRIMARY RENOVATIONS (ORIGINAL SCOPE & NEW ADDITION TIMELINE)

Northeast High School has completed its weight room renovations and all equipment has been installed. Restroom and culinary lab renovations are underway in Building 3 and roofing repairs have begun on Building 12.

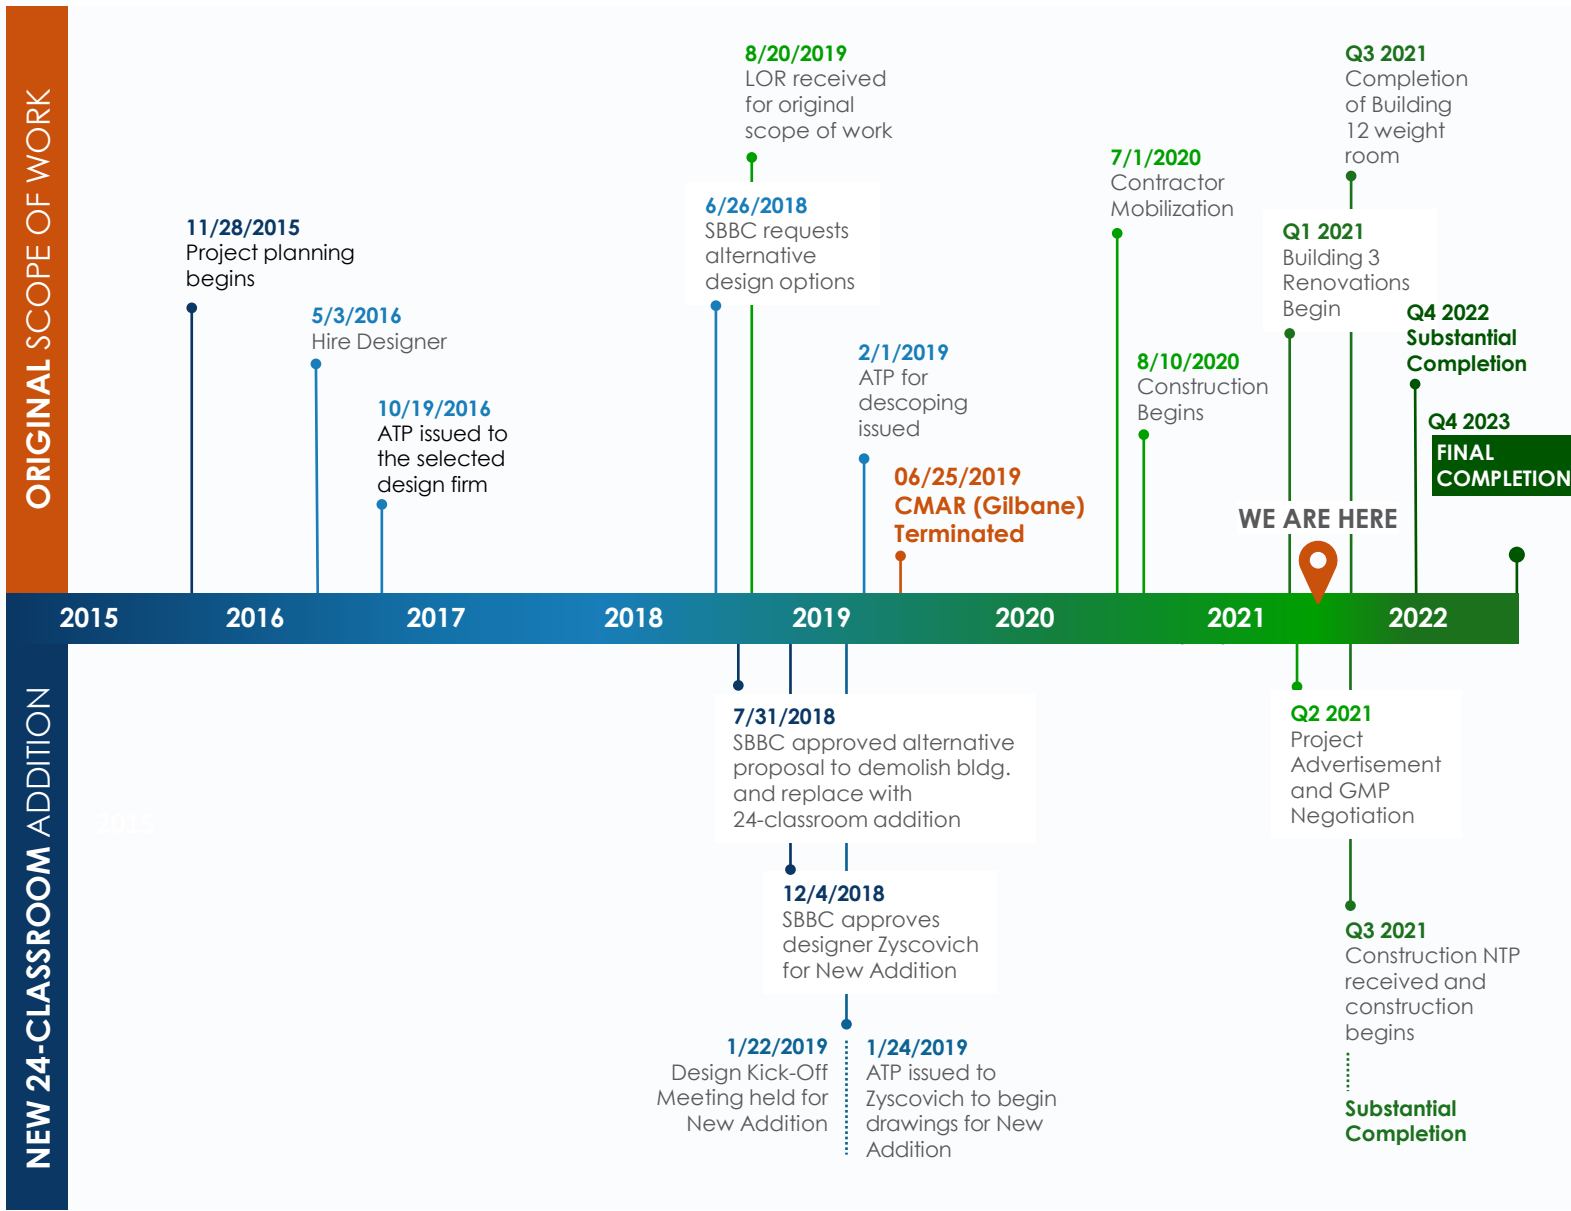



NORTHEAST HIGH SCHOOL

PRIMARY RENOVATIONS (PHASE 1)



ACTIVE CONSTRUCTION



WORK COMPLETED

✓ WEIGHT ROOM RENOVATIONS



WORK IN PROGRESS

BUILDING 1

- Science Lab

BUILDING 3

- STEM Lab, Culinary lab, restroom & fire protection

BUILDING 12

- Fire alarm, roofing





NORTHEAST HIGH SCHOOL

PRIMARY RENOVATIONS (PHASE 1)

WORK IN PROGRESS



BLDG. 8 ROOFING COMPLETE



BLDG. 3 ROOFING UNDERWAY



FIRE MAIN TIE-IN



INDUSTRIAL/CULINARY LAB



INDUSTRIAL/CULINARY LAB



INDUSTRIAL/CULINARY LAB



RESTROOM RENOVATION



INDUSTRIAL/CULINARY LAB



UNDERGROUND FIRE PROTECTION



NORTHEAST HIGH SCHOOL

NEW CLASSROOM ADDITION (PHASE 2)



DESIGN

Design drawings are being reviewed by the Building Department for the new classroom addition.

SCHOOL CHOICE ENHANCEMENT PROGRAM




IMPLEMENTATION

The school has elected to hold on to the remaining dollars until the Primary Renovations are complete.

ITEMS DELIVERED AND INSTALLED:

- ✓ Outdoor trash receptacles
- ✓ Science equipment
- ✓ Golf carts
- ✓ Scoring tables
- ✓ Digital marquee
- ✓ Gym scoreboards (2)
- ✓ Football scoreboard
- ✓ Electric strikes (2)
- ✓ Standalone door alarms
- ✓ Window wraps





SCHOOLS IN YOUR COMMUNITY

SCHOOL	PROJECT PHASE
James S. Rickards Middle School	ACTIVE CONSTRUCTION
Lloyd Estates Elementary School	HIRE CONTRACTOR
North Andrews Gardens Elementary School	PROJECT DESIGN
Oakland Park Elementary School	ACTIVE CONSTRUCTION

JAMES S. RICKARDS MIDDLE SCHOOL



Address	6000 NE 9 AVENUE, OAKLAND PARK 33334
Location Number	2121
Board District	3
Board Member	Sarah Leonardi
ADEFP Budget	\$10,981,080
Total Facilities Budget	\$10,558,080

PRIMARY RENOVATIONS

CURRENT PHASE

ACTIVE CONSTRUCTION

PROJECT UPDATE

Construction is on-going in buildings 2 and 5. Site work on-going. Forensic engineering analysis continues, shoring and selective demolition in building 1 in the area of the collapse has begun.

PROJECT SCOPE

Additional Funding - Board Approved 09/17/19 (JJ-1)	\$5,449,080
Building Envelope Improvements	\$2,058,000
Electrical Improvements	\$353,000
Fire Alarm	\$461,000
Fire Sprinklers	\$13,000
HVAC Improvements	\$1,339,654
Media Center Improvements	\$441,000
Safety / Security Upgrade	\$108,000
Scope Modification – Chiller Replacement (Complete)	\$235,346

2020 RESET SCHEDULE (CALENDAR YEAR)

PROJECT PLANNING

Q1 2016 - Q1 2016

HIRE DESIGNER

Q1 2016 - Q3 2016

PROJECT DESIGN

Q3 2016 - Q1 2019

HIRE CONTRACTOR

Q2 2017 - Q4 2019

ACTIVE CONSTRUCTION

Q4 2019 - Q3 2022

CONSTRUCTION CLOSEOUT

Q3 2022 - Q4 2022

ORIGINAL SCHEDULE Q3 2019

2018 SCHEDULE Q1 2021

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Floor Mats	Dehumidifier
Outdoor Metal Bleachers	Laptops
Flat Screen TVs	Tables For Teacher's Lounge
Clay Extruder	Chairs
Two-way Radios	Laminator
Indoor Furniture	Electric Strike
Projectors	Digital Marquee

BUDGET

\$100,000

SCHEDULE

(CALENDAR YEAR)

PLANNING / DESIGN

Q1 2016 (Actual: 01/2016)

IMPLEMENTATION

Q2 2017 (Actual: 04/2017)

COMPLETE

Q1 2020 (Actual: 02/2020)

TECHNOLOGY



COMPLETE

SCOPE

496 Items Delivered

FLAG:

COMMENTS:

LLOYD ESTATES ELEMENTARY SCHOOL



Address	750 NW 41 STREET, OAKLAND PARK 33309
Location Number	1091
Board District	3
Board Member	Sarah Leonardi
ADEFP Budget	\$2,581,000
Total Facilities Budget	\$2,352,000

PRIMARY RENOVATIONS

CURRENT PHASE

HIRE CONTRACTOR

PROJECT UPDATE

The school is in the process of hiring a contractor to complete its renovations.

PROJECT SCOPE

Building Envelope Improvements	\$625,000
Fire Alarm	\$293,000
Fire Sprinklers	\$280,000
HVAC Improvements	\$870,000
Media Center Improvements	\$184,000

2020 RESET SCHEDULE (CALENDAR YEAR)

PROJECT PLANNING

Q2 2016 - Q3 2016

HIRE DESIGNER

Q2 2016 - Q1 2017

PROJECT DESIGN

Q1 2017 - Q4 2020

HIRE CONTRACTOR

Q2 2018 - Q3 2021

ACTIVE CONSTRUCTION

Q3 2021 - Q1 2024

CONSTRUCTION CLOSEOUT

Q1 2024 - Q2 2024

ORIGINAL SCHEDULE Q2 2019

2018 SCHEDULE Q1 2021

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

COMPLETE

DELIVERED

Two-way Radios
 Poster Maker
 LCD Projectors
 Digital Cameras
 Recordex

BUDGET

\$100,000

SCHEDULE (CALENDAR YEAR)

PLANNING / DESIGN

Q1 2016 (Actual: 01/2016)

IMPLEMENTATION

Q4 2016 (Actual: 11/2016)

COMPLETE

Q1 2017 (Actual: 03/2017)

MUSIC



COMPLETE

SCOPE

390 Instruments delivered

TECHNOLOGY



COMPLETE

SCOPE

253 Items Delivered

FLAG:

COMMENTS:

NORTH ANDREWS GARDENS ELEMENTARY SCHOOL



Address	345 NE 56 STREET, OAKLAND PARK 33334
Location Number	0521
Board District	3
Board Member	Sarah Leonardi
ADEFP Budget	\$2,747,000
Total Facilities Budget	\$2,378,000

PRIMARY RENOVATIONS

CURRENT PHASE

PROJECT DESIGN

PROJECT UPDATE

Drawings are being developed by a professional design team. Once complete, a contractor will be hired to begin construction.

PROJECT SCOPE

Building Envelope Improvements	\$1,263,000
Fire Sprinklers	\$18,000
HVAC Improvements	\$997,000

2020 RESET SCHEDULE (CALENDAR YEAR)

PROJECT PLANNING

Q2 2017 - Q3 2017

HIRE DESIGNER

Q3 2017 - Q3 2019

PROJECT DESIGN

Q2 2018 - Q3 2021

HIRE CONTRACTOR

Q3 2021 - Q3 2022

ACTIVE CONSTRUCTION

Q3 2022 - Q4 2024

CONSTRUCTION CLOSEOUT

Q4 2024 - Q1 2025

ORIGINAL SCHEDULE Q3 2020

2018 SCHEDULE Q4 2021

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

IMPLEMENTATION

DELIVERED

Aiphone Thinkpads
 Submaster Think Stations
 Golf Cart EarthWalk
 ID Maker Carts
 Laptops Projectors
 Elmo
 Document Cameras
 Executive Chairs

BUDGET

\$100,000

IN PROGRESS

Trash Receptacles

SCHEDULE

(CALENDAR YEAR)

PLANNING / DESIGN

Q4 2018 (Actual: 11/2018)

IMPLEMENTATION

Q2 2019 (Actual: 05/2019)

COMPLETE

TBD

MUSIC



COMPLETE

SCOPE

126 Instruments Delivered

TECHNOLOGY



COMPLETE

SCOPE

382 Items Delivered

FLAG:

COMMENTS:

OAKLAND PARK ELEMENTARY SCHOOL



Address	936 NE 33 STREET, OAKLAND PARK 33334
Location Number	0031
Board District	3
Board Member	Sarah Leonardi
ADEFP Budget	\$6,180,330
Total Facilities Budget	\$5,862,330

PRIMARY RENOVATIONS

CURRENT PHASE

ACTIVE CONSTRUCTION

PROJECT UPDATE

Air handling units have been installed in Buildings 1 and 13, and the existing roof has been demolished on Building 10. The installation of exterior light fixtures and temporary roofs remain ongoing.

PROJECT SCOPE

Additional Funding - Board Approved 12/10/19 (JJ-3)	\$2,701,330
Building Envelope Improvements	\$975,000
Electrical Improvements	\$845,000
Fire Alarm	\$50,000
HVAC Improvements	\$1,191,000

2020 RESET SCHEDULE

(CALENDAR YEAR)

PROJECT PLANNING

Q4 2016 - Q4 2016

HIRE DESIGNER

Q4 2016 - Q3 2017

PROJECT DESIGN

Q4 2017 - Q2 2019

HIRE CONTRACTOR

Q3 2018 - Q1 2020

ACTIVE CONSTRUCTION

Q1 2020 - Q1 2023

CONSTRUCTION CLOSEOUT

Q1 2023 - Q1 2023

ORIGINAL SCHEDULE Q4 2019

2018 SCHEDULE Q4 2020

SCHOOL CHOICE ENHANCEMENT (SCEP)

CURRENT PHASE

IMPLEMENTATION

DELIVERED

Playground Upgrades
Murals

BUDGET

\$100,000

IN PROGRESS

Media Center Carpet

SCHEDULE

(CALENDAR YEAR)

PLANNING / DESIGN

Q4 2016 (Actual: 12/2016)

IMPLEMENTATION

Q2 2017 (Actual: 05/2017)

COMPLETE

TBD

MUSIC



COMPLETE

SCOPE

1,655 Instruments Delivered

TECHNOLOGY



COMPLETE


SCOPE

259 Items Delivered

FLAG:

COMMENTS:

STAY CONNECTED



BCPSSMARTFUTURES.COM

The new SMART Program website serves as an accessible, easy to use, comprehensive place for school communities and key stakeholders to find information about all SMART projects and the latest happenings in the Program.

 <https://bcpssmartfutures.com/oaklandpark/>

